

Monkey-Head-Project Repo Restructure Migration Plan

Executive summary

Enabled connectors (used first): `github` (repo: `DylanLRPollock/Monkey-Head-Project`).

This report produces a practical, engineer-ready **repository restructuring to-do list** that prioritizes: (a) making the Python runtime importable and CI-green, (b) separating “runtime code” from “platform/packaging artifacts” and “canon content,” and (c) setting the team up for a controlled **staging → pre-release (v84.3-pre) → freeze → rewrite** cycle already described in the repo’s operating docs. The repo currently includes a Python package declared as `hueyos` with `requires-python = ">=3.13,<3.15"` and console scripts, including `huey-api = "huey.api:main"`. ¹ The most urgent structural flaw is that a large portion of the intended `hueyos` package appears to live under **invalid Python package directory names** (notably `src/ai-os/`), while tests and runtime modules import `hueyos.*`, which creates avoidable breakage and complicates the upcoming rewrite. ² ³

This plan is **deployable as a migration sequence**: it includes a proposed taxonomy, explicit file/folder actions (keep/move/rename/rewrite/delete), sample `git` commands, CI updates, rollback rules, and verification/acceptance criteria.

Assumptions (explicit, per request; no clarifying questions): - Default branch is `main`, and restructuring work is performed via feature branches merged back to `main`. CI currently runs on `main` and `develop`. ⁴ - Where a file/folder is not discoverable in the sampled listings, it’s labeled **UNSPECIFIED** (not assumed absent forever). - Any “exact port”, “credential”, “serial protocol”, “GPIO map”, etc. not present in repo text is treated as **UNSPECIFIED**. - This report lists **high-value, discovered paths** and provides a deterministic script workflow to produce a complete inventory (`git ls-files`) before executing bulk `git mv` operations.

Current repository map as discovered

The repository self-identifies as “Monkey-Head-Project / HueyOS” with a Python package name `hueyos` and a master plan spec file `master-plan-v23.json`. ⁵ Key runtime environment settings are documented in `huey.env.example` (e.g., `HUEY_HOST`, `HUEY_PORT=1995`, `HUEY_ROOT`, `HUEY_MEMORY_ROOT`, local model backend settings like `OLLAMA_PORT=11434`). ⁶ Docker Compose also defaults to `HUEY_PORT=1995` and uses Compose **profiles** (`worker`, `extras`) for optional services like Redis. ⁷ ⁸

Current top-level map and key contents

Current path	Type	Key discovered files/ subpaths	Purpose & notes	Action (summary)
<code>.github/</code>	dir	<code>.github/workflows/ci.yml</code> , <code>.github/workflows/codeql.yml</code> , <code>.github/dependabot.yml</code> ⁴ ⁹ ¹⁰	CI uses Python 3.13 and runs <code>make lint</code> + <code>make coverage</code> . ⁴	Keep , update paths/rules after moves
<code>.disk/</code>	dir	<code>.disk/mkisofs</code> ¹¹	ISO/build artifact surface (likely platform/ISO root metadata).	Move under <code>platform/iso/</code> (recommended)
<code>README.md</code>	file	(root) ⁵	Authoritative narrative + doctrine + repo map + deployment flow.	Keep , update after restructure
<code>pyproject.toml</code>	file	(root) ¹	Declares package <code>hueyos</code> , scripts, requires-python, dependencies/extras.	Keep, rewrite sections to match new module reality
<code>Makefile</code>	file	(root) ¹²	Runs <code>uvicorn huey.api:app</code> , coverage includes <code>--cov=huey</code> <code>--cov=hueyos</code> .	Keep , update run target and coverage if needed
<code>requirements.txt</code> / <code>constraints.txt</code>	files	(root) ¹³ ¹⁴	Large pinned set; <code>constraints.txt</code> is currently “intentionally empty.” ¹⁴	Keep , clarify roles vs <code>pyproject.toml</code>
<code>SECURITY.md</code>	file	(root) ¹⁵	Repo security policy, OS baseline claims, disclosure process.	Keep , update any drift
<code>LICENSE</code>	file	(root) GPLv3 text ¹⁶	Code is GPL-3.0-only; README claims docs/media are CC-BY-SA-4.0. ⁵	Keep

Current path	Type	Key discovered files/ subpaths	Purpose & notes	Action (summary)
docs/	dir	docs/index.md, docs/api-reference.md, docs/governance.md, docs/orchestrator-deployment.md, docs/security-maintenance-audit.md, docs/repository-restructure-*.md 17 18 19 20 21 22 23	The docs already include a restructure recommendation and inventory checklist. 22	Keep , update path references after moves
infra/	dir	infra/docker/docker-compose.yml, infra/docker/Dockerfile, infra/docker/docker/orchestrator_utils.py, infra/docker/docker/hostos/hostos.py 7 24 25 26	Compose uses profiles + env-file; Dockerfile currently installs pygpt-net, creating mismatch with HueyOS runtime expectations. 24 7	Rewrite Docker build surfaces; keep orchestrators
platform/	dir	platform/boot/..., platform/packaging/dists/..., platform/installers/... 27 28 29	OS/ISO/debian artifacts and installers are already consolidated here.	Keep , enforce "platform-only" boundaries
archives/	dir	archives/releases/... + checksums 30	Release blobs and checksums preserved.	Keep , standardize naming and manifest
src/	dir	src/huey/..., src/ai-os/..., plus large "canon"/memory content under src/huey/memory/... 31 2 32	Core technical debt zone: invalid python directory names and duplicated/compat layers.	Major restructure (P0)
tests/	dir	tests/test_api_routes.py, tests/test_cli.py, tests/test_hostos_module.py etc. 3 33 34	Tests assume hueyos.* imports exist. 3	Keep , update imports and fixtures after moves

Current path	Type	Key discovered files/subpaths	Purpose & notes	Action (summary)
<code>apps/</code>	dir	<code>apps/huey-gui/</code> <code>__init__.py</code> , <code>apps/huey-gui/main_ui.py</code> 35 36	“Apps” includes another invalid python package dir name (<code>huey-gui</code> with <code>__init__.py</code>). 37	Rename to valid package dir
<code>integrations/</code>	dir	<code>integrations/pygpt/py-gpt/...</code> , <code>integrations/pygpt/pygpt-mhp/...</code> 38 39	Large integrated upstream(s). Should be isolated from HueyOS packaging and CI scope.	Keep , sandbox via CI excludes

UNSPECIFIED top-level paths (mentioned in ignore rules or README but not discovered in the sampled listings): `assets/`, `media/`, `vendor/`, `wiki/`. Treat as “may exist or may be planned” until verified.

Proposed canonical taxonomy and naming rules

The repo already includes a strong “recommended top-level layout” in `docs/repository-restructure-recommendation.md`. 22 This migration plan adopts that structure, with one critical addition: a hard rule that **every importable Python package directory must be a valid Python identifier** (no hyphens), consistent with `src`-layout packaging expectations. 40

Canonical folder taxonomy

New canonical path	What belongs here	Boundaries/ownership	Notes
<code>src/hueyos/</code>	Canonical HueyOS runtime (importable)	Runtime engineering	Replace invalid <code>src/ai-os/</code> with <code>src/hueyos/</code> (rename) while keeping compatibility shims as needed. 2
<code>src/huey/</code>	Compatibility namespace (<code>huey</code> CLI imports, transitional bridges)	Runtime engineering	Keep <code>huey</code> as a shim layer as long as <code>pyproject.toml</code> scripts expose <code>huey = "huey.cli:main"</code> . 1
<code>apps/</code>	Human-invoked apps (GUI, dashboards)	Product/UI	If python-importable, directories must be valid (e.g., <code>apps/huey_gui/</code>). 37

New canonical path	What belongs here	Boundaries/ ownership	Notes
<code>infra/</code>	Docker/compose, orchestrators, CI helper scripts	Ops/infra	Compose profiles should remain for optional services. ⁷ ⁴¹
<code>platform/</code>	OS/boot/installers/ debian artifacts	Platform/OS	Debian packaging docs distinguish source-vs-binary structure; keep platform artifacts out of <code>src/</code> . ⁴²
<code>docs/</code>	Specs, governance, runbooks, audit reports	Docs/ governance	Update hardcoded paths/ports (e.g., orchestrator doc paths) after moving. ²⁰
<code>archives/</code>	Frozen releases, checksums, snapshots	Release engineering	Enforce “no active development” here; only archives and integrity manifests. ³⁰
<code>integrations/</code>	Vendored/upstream integrations	Integrations	Exclude from HueyOS packaging by default; optionally make them Git submodules later (UNSPECIFIED). ³⁹
<code>tests/</code>	Unit/integration tests	QA	CI runs pytest + coverage. ⁴


Naming rules to enforce in the rewrite branch

- **Importable python packages:** must be valid identifiers (e.g., `hueyos`, `huey_gui`), not hyphenated directories. This aligns with standard `src`-layout expectations and prevents accidental import failures. ⁴⁰
- **Compose:** keep “profiles” for optional components; do not silently enable a service when its profile isn’t selected (Compose can error or ignore). ⁴¹
- **Docker images:** use Dockerfile best practices (multi-stage builds, least privilege) for production images. ⁴³
- **pyproject entry points:** console scripts must point to real callables (`[project.scripts]` semantics). ⁴⁴

Ordered migration plan with file-level actions, priorities, and commands

This section is the deployable “do this in order” plan. It aligns with: **staging** → **pre-release (v84.3-pre)** → **freeze** → **rewrite** (already described in repo narrative) while focusing specifically on repository structure and import integrity. ⁵

Module connectivity diagram

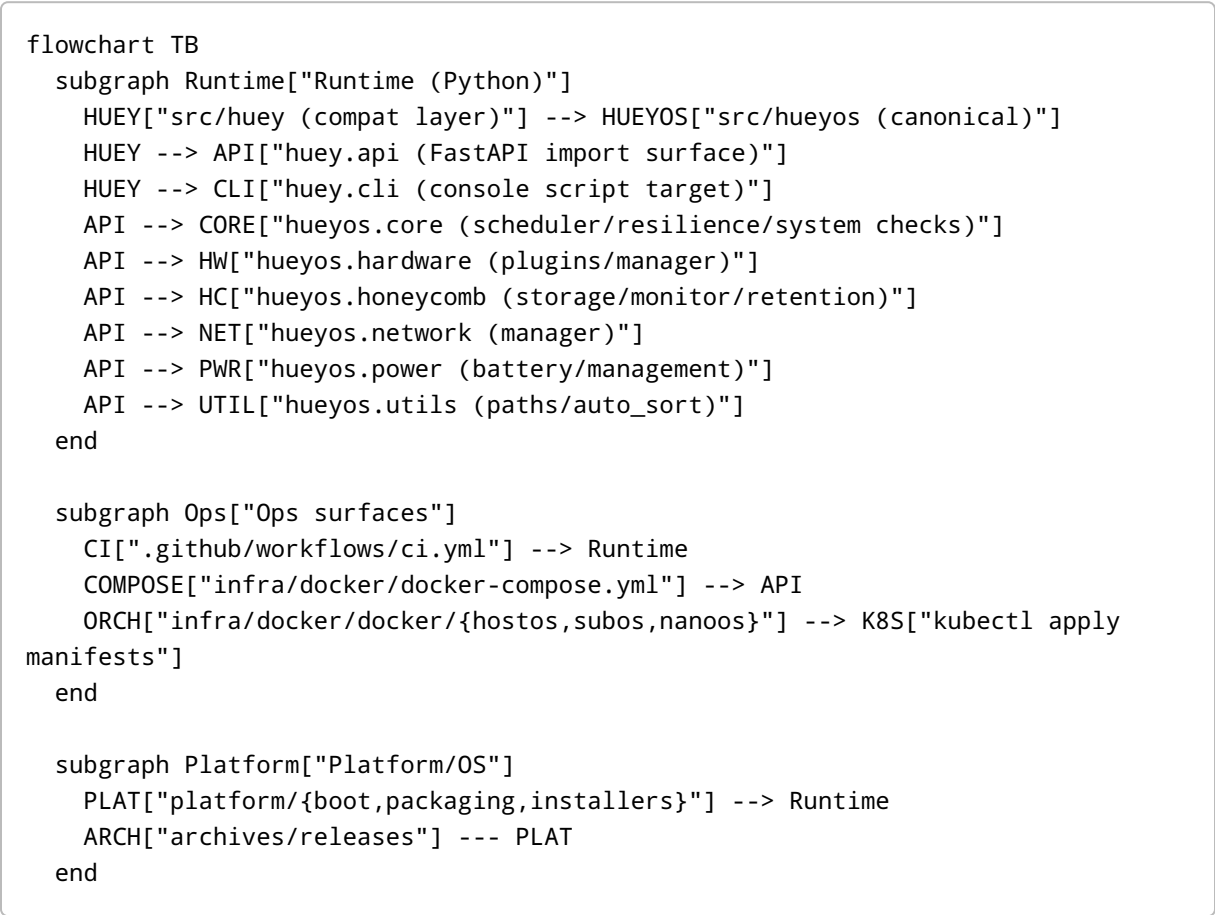

This diagram reflects existing interfaces: CI runs `make lint` / `make coverage` on Python 3.13. ⁴ The FastAPI surface is documented under `docs/api-reference.md`, but its examples assume `uvicorn huey.api:app` and show port 8000 while operational defaults elsewhere are 1995—treat any inconsistent port mention as “must reconcile.” ¹⁸ ⁶ ¹²

Migration steps table

Step	Scope	Action type	Priority	Effort	Sample commands (illustrative)	Ro
Preflight snapshot	Whole repo	Archive + inventory	P0	S	<code>git checkout main && git pull</code> <code>git tag v84.3-pre-freeze-candidate</code> (name UNSPECIFIED) <code>git ls-files > .migration/current-file-list.txt</code>	If a res re <t .n art bra

Step	Scope	Action type	Priority	Effort	Sample commands (illustrative)	Ro
Fix invalid Python package root	<code>src/ai-os/</code> → <code>src/hueyos/</code>	Rename	P0	M	<code>git mv "src/ai-os" src/hueyos</code>	If i rev (g an cor (be
Fix invalid app package dir	<code>apps/huey-gui/</code>	Rename	P1	S	<code>git mv "apps/huey-gui" apps/huey_gui</code>	Re do de kee RE on
Repair console-script entrypoint mismatch	<code>huey-api</code> entry point	Rewrite	P0	M	In <code>pyproject.toml</code> : change to <code>huey-api = "hueyos.api:main"</code> or implement <code>def main() in huey/api.py</code>	If n sta the firs pa lat
Normalize package discovery & metadata	<code>pyproject.toml</code>	Rewrite	P0	S	Ensure <code>[tool.setuptools.packages.find]</code> only finds valid packages under <code>src/</code> 1	Re cor if b
Align Makefile coverage/run	<code>Makefile</code>	Rewrite	P0	S	Update <code>coverage</code> to match actual packages after rename; run target should remain <code>uvicorn ... --host --port</code> (Uvicorn settings) 12 45	Re cor
Split Docker build targets	<code>infra/docker/Dockerfile</code>	Split + rewrite	P0	M	Create <code>infra/docker/Dockerfile.hueyos</code> (HueyOS) and <code>infra/docker/Dockerfile.pygpt</code> (optional); update compose <code>dockerfile:</code> accordingly 24 7	Ke Do in pin "le
Update orchestrator docs paths	<code>docs/orchestrator-deployment.md</code>	Rewrite	P1	S	Paths currently show <code>python3 docker/hostos/...</code> but code lives in <code>infra/docker/docker/...</code> ; update docs accordingly 20	If o cor pa ad loc

Step	Scope	Action type	Priority	Effort	Sample commands (illustrative)	Ro
Move “canon/ memory TXT” out of import packages	<code>src/huey/ memory/TXT/...</code>	Move	P1	L	<code>git mv src/huey/memory/TXT docs/ canon/TXT</code> (exact destination taxonomy UNSPECIFIED) ³²	Ar str an sn <d mo
Reduce duplicate implementations	<code>src/huey/*</code> vs <code>src/hueyos/*</code>	Merge + delete	P1	L	Choose canonical modules (prefer <code>hueyos.*</code>), keep <code>huey.*</code> thin proxies for one cycle (per repo restructure inventory) ²³	Ro me pro de
CI path tightening	<code>.github/ workflows/*</code>	Rewrite	P1	S	Add CI job: “structure check” (no hyphenated importable packages; no <code>src/*</code> folders with invalid names) ⁴	Re cor ho lat
Freeze gate	Whole repo	Policy	P0	S	Tag + branch protection: “freeze = bugfix/ security only” (names UNSPECIFIED)	If f bro cha rol

Major move scripts and “bulk rename” safety

Before any bulk `git mv`, run `git ls-files` inventory and store it in a versioned directory (e.g., `.migration/`). This is how you satisfy “complete file list” deterministically without relying on manual enumeration.

```
# One-time inventory snapshot (run from repo root)
mkdir -p .migration/inventory
git ls-files > .migration/inventory/git-ls-files.main.txt

# Optional: categorize for review
grep '^src/' .migration/inventory/git-ls-files.main.txt > .migration/inventory/
src-files.txt
grep '^platform/' .migration/inventory/git-ls-files.main.txt > .migration/
inventory/platform-files.txt
```

This approach is consistent with the repo’s own stated guardrail: “perform moves in small batches with a path-mapping changelog.” ²²

CI, packaging, and deployment implications

Python packaging and entry points

The project declares console scripts under `[project.scripts]`.¹ Under PEP 621, these map to `console_scripts` entry points and must reference a valid importable callable.⁴⁴ The repo's security/maintenance audit explicitly flags that `huey-api = "huey.api:main"` is currently mismatched because `src/huey/api.py` is a compatibility wrapper and does not define `main`.²¹ Therefore, the restructure must include one of: - implement a real `main()` callable in the target module, or - repoint the script to an existing callable that exists after restructure (`hueyos.api:main`, path UNSPECIFIED until created).

Additionally, the repository uses a `src` layout (packages under `src/`), which is a recognized packaging pattern for avoiding accidental imports from the working directory.⁴⁰ This strengthens the argument that `src/ai-os/` must be renamed to a valid package directory (`src/hueyos/`).

Docker and Compose

`infra/docker/docker-compose.yml` uses Compose profiles (`worker`, `extras`) and sets defaults via an anchor `x-service-defaults`.⁷ Compose profiles behave such that services without a matching active profile are ignored unless explicitly targeted.⁴¹ This structure should be preserved, but the **build target must be corrected** because the current `infra/docker/Dockerfile` installs and runs `pygpt-net`, not HueyOS.²⁴

For the rewrite, follow Docker's published best practices: multi-stage builds, minimizing dependencies in final image, and using `USER` (non-root) where possible.⁴³

Debian/platform packaging

The `platform/` directory already includes boot and packaging artifacts (e.g., `platform/packaging/dists/...`).²⁸ Debian's policy docs distinguish the structure of Debian source packages (with a `debian/` directory controlling builds) from raw binary/package artifacts.⁴² In restructure terms: - keep "distribution artifacts" inside `platform/` or `archives/`, - prevent those artifacts from being treated as importable runtime code, CI lint scope, or Python packaging inputs.

Uvicorn/FastAPI runtime settings

The Makefile runs `uvicorn huey.api:app --host 0.0.0.0 --port 1995`.¹² Uvicorn's own documentation confirms these CLI settings (`--host`, `--port`, `--reload`, `--workers`, env controls) are first-class configuration mechanisms.⁴⁵ Any restructure must maintain a stable import path for the ASGI app target (`module:app`) and avoid breaking the runtime invocation pattern.

Rollback, archival policy, and final verification

Rollback and archival policy per change class

- **Renames/moves** (`git mv`): treat each “batch move” as a single commit with an explicit mapping in commit message. If a move breaks CI, rollback should be `git revert <move-commit>` to restore exact file paths, not partial manual edits.
- **Structural rewrites (pyproject/entry points, Docker builds)**: require a paired rollback artifact:
 - a tag (e.g., `v84.3-pre-freeze-candidate`, exact name UNSPECIFIED),
 - and a preserved copy of old configs in `archives/config-snapshots/<date>/...` (path naming UNSPECIFIED).
- **Canon and long text archives**: *never delete outright*. Move to `archives/` or `docs/canon/` and keep a manifest file (e.g., `archives/canon-snapshots/<date>/MANIFEST.txt`, UNSPECIFIED exact path). This matches the repo’s doctrine that resets are “audited forks,” not silent amnesia. ⁵

Final verification checklist

Category	Check	Command / method	Pass criteria
Repo structure	No invalid importable package dirs under <code>src/</code>	<code>python -c "import hueyos; import huey"</code>	Imports succeed
Entry points	Console scripts resolve	<code>python -c "import importlib; importlib.import_module('huey.cli')"</code>	No ImportError
API boot	Uvicorn can boot app	<code>make run</code> ¹²	Server starts
Health endpoint	<code>/healthz</code> responds	<code>curl -fsS http://127.0.0.1:1995/healthz</code>	200 + expected JSON (shape per docs/tests) ¹⁸
CI	GitHub Actions green	Check CI workflow	<code>lint</code> + <code>tests</code> jobs pass ⁴
Coverage	Coverage doesn’t fail due to missing pkg	<code>make coverage</code> ⁴	Coverage report produced
Docker	Compose builds correct image	<code>cd infra/docker && docker compose build</code> ⁷	HueyOS image builds (not pygpt-only)

Category	Check	Command / method	Pass criteria
Docs	Paths/ports reflect reality	manual review of <code>docs/index.md</code> , <code>docs/orchestrator-deployment.md</code> , <code>docs/api-reference.md</code> ¹⁷ ²⁰ ¹⁸	No contradicted “how to run” instructions
Security gate	Audit action items addressed or explicitly deferred	<code>docs/security-maintenance-audit.md</code> checklist ²¹	P0 security notes tracked

Acceptance criteria

The restructure is successful (for the v84.3-pre / freeze bridge) when all of the following are true:

- `pyproject.toml` entry points correspond to actual callable targets (PEP 621 requirement for scripts) and CI can install `pip install -e .[dev]` and run lint/tests. ⁴ ⁴⁴
- The canonical HueyOS namespace is importable as `hueyos` (matching the declared distribution name), and the old `huey` namespace is either compatible or explicitly documented as transitional. ¹
- Docker Compose builds and runs the HueyOS runtime image (not an unrelated `pygpt-net` -only image), while preserving Compose profiles behavior. ⁷ ⁴¹
- “Platform artifacts” remain clearly partitioned under `platform/` / `archives/`, consistent with Debian packaging concepts of keeping packaging/build system structure separate from application runtime code. ²⁸ ⁴²
- The migration is reversible via tags + revert commits, and the repo retains continuity-of-record (archive snapshots rather than deletions), consistent with the repo's own reset/continuity doctrine. ⁵

¹ `pyproject.toml`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/pyproject.toml>

² `__init__.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/src/ai-os/__init__.py

³ `test_api_routes.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/tests/test_api_routes.py

⁴ `ci.yml`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/.github/workflows/ci.yml>

⁵ `README.md`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/README.md>

⁶ `huey.env.example`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/huey.env.example>

7 **docker-compose.yml**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/infra/docker/docker-compose.yml>

8 41 **<https://docs.docker.com/reference/compose-file/profiles/>**

<https://docs.docker.com/reference/compose-file/profiles/>

9 **codeql.yml**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/.github/workflows/codeql.yml>

10 **dependabot.yml**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/.github/dependabot.yml>

11 **.disk/mkisofs**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/.disk/mkisofs>

12 **Makefile**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/Makefile>

13 **requirements.txt**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/requirements.txt>

14 **constraints.txt**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/constraints.txt>

15 **SECURITY.md**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/SECURITY.md>

16 **LICENSE**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/LICENSE>

17 **index.md**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/docs/index.md>

18 **api-reference.md**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/docs/api-reference.md>

19 **governance.md**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/docs/governance.md>

20 **orchestrator-deployment.md**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/docs/orchestrator-deployment.md>

21 **security-maintenance-audit.md**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/docs/security-maintenance-audit.md>

22 **repository-restructure-recommendation.md**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/docs/repository-restructure-recommendation.md>

23 **repository-restructure-inventory.md**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/docs/repository-restructure-inventory.md>

24 **Dockerfile**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/infra/docker/Dockerfile>

25 **api.py**

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/src/huey/api.py>

26 `__init__.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/src/huey/__init__.py

27 `platform/boot/grub/grub/live-theme/theme.txt`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/platform/boot/grub/grub/live-theme/theme.txt>

28 `platform/packaging/dists/forky/Release`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/platform/packaging/dists/forky/Release>

29 `platform/installers/debian/sources.list`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/platform/installers/debian/sources.list>

30 `archives/releases/checksums/sha256sum.txt`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/archives/releases/checksums/sha256sum.txt>

31 `archives/releases/hueyos-6.18.5/6.18.5-hueyos.iso.sha256`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/archives/releases/hueyos-6.18.5/6.18.5-hueyos.iso.sha256>

32 `src/huey/memory/TXT/1) Monkey Head Project [Thesis].txt`

[https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/src/huey/memory/TXT/1\)%20Monkey%20Head%20Project%20\[Thesis\].txt](https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/src/huey/memory/TXT/1)%20Monkey%20Head%20Project%20[Thesis].txt)

33 `test_cli.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/tests/test_cli.py

34 `test_hostos_module.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/tests/test_hostos_module.py

35 `apps/huey-gui/__init__.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/apps/huey-gui/__init__.py

36 `apps/huey-gui/main_ui.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/apps/huey-gui/main_ui.py

37 `__init__.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/main/apps/huey-gui/__init__.py

38 `integrations/pygpt/py-gpt/README.md`

<https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/integrations/pygpt/py-gpt/README.md>

39 `integrations/pygpt/pygpt-mhp/src/pygpt_net/app.py`

https://github.com/DylanLRPollock/Monkey-Head-Project/blob/430ebb3daf6bd5b129ffae6e2a6c8a08e08b2331/integrations/pygpt/pygpt-mhp/src/pygpt_net/app.py

40 `https://packaging.python.org/en/latest/discussions/src-layout-vs-flat-layout/`

<https://packaging.python.org/en/latest/discussions/src-layout-vs-flat-layout/>

42 `https://www.debian.org/doc/debian-policy/ch-source`

<https://www.debian.org/doc/debian-policy/ch-source>

⁴³ https://docs.docker.com/develop/develop-images/dockerfile_best-practices/
https://docs.docker.com/develop/develop-images/dockerfile_best-practices/

⁴⁴ <https://peps.python.org/pep-0621/>
<https://peps.python.org/pep-0621/>

⁴⁵ <https://www.uvicorn.org/settings/>
<https://www.uvicorn.org/settings/>
